

CLOSURE & HANDOVER | ORGANIZATIONAL PROCESS ASSETS

Saudi Elaf Cross-Functional Processes Development Project

A part of Saudi Elaf's Organizational Process Assets is developed, approved and ready for formal handover

SAUDI ELAF COMPANY

Client and beneficiary

ENG. AMR ELHADARY

Personal outsourced technical delivery

ALL PROCESS PACKAGES APPROVED MAY 2025

Final executive presentation | Controlled document | Saudi Elaf internal use | July 2026 | Rev.0

The processes were developed and their implementation supported as an outsourced technical scope

01

SAUDI ELAF COMPANY

Client and beneficiary

Owner of the requirement and of the handed-over process system



02

ENG. AMR ELHADARY

Personal outsourced technical delivery

Led the diagnosis, design, implementation, monitoring and closure of the outsourced scope

TECHNICAL SCOPE

- Diagnosis of the current operating state
- Cross-functional process design and interdepartmental role definition
- Support of the implementation through Email, Jisr and Odoo
- Monitoring, tuning, closure and handover

SCOPE EXCLUSION

- Departmental SOPs, policies and detailed templates are developed, issued and maintained by the responsible department manager
- They are cross-referenced only where a process depends on them
- No financial case, contract value, invoice or settlement content is presented

The gap analysis defined the current-to-future roadmap and seeded ERP transformation

01

DIAGNOSE

Gap analysis, SWOT, interviews, document, tool and integration review

02

DESIGN

Cross-functional workflows and RASCI role interfaces

03

IMPLEMENT

Email, Jisr and Odoo application, then monitoring and tuning

04

HAND OVER

Record, repository, ownership transfer and formal closure

Revision 3 technical proposal dated 29 April 2024. The findings defined the requirements needed to move Saudi Elaf from its current state to the intended future operating state, and became the initial seed for ERP transformation.

Documented gaps and interviews defined the cross-functional requirements

17

DISTINCT INTERVIEW SESSIONS

18

CONTROLLED MOM FILES

12

FUNCTIONS AND PROJECTS COVERED

RECORD INPUTS

Interviews, records and forms, tool and system review, project and site input, management direction



GAP ANALYSIS

Gaps, duplication, unclear roles, missing documentation and control weaknesses



FUTURE-STATE DESIGN

Approved workflow and RASCI, clarified role interfaces, ERP foundation

The interview program covered all then-relevant key persons and department stakeholders. It comprised 17 distinct sessions, each recorded by one controlled MOM record held at its latest revision.

Progress advanced from early design to full approval and application



2025 - 2026 APPLICATION · MONITORING · TUNING · HANDOVER

PROGRESS RECONCILIATION

The July and August figures measure design development; the November figure is approval-weighted technical progress. They are not one continuous percentage. May 2025 is the governing approval point for all process packages.

The project delivered a part of Saudi Elaf's controlled Organizational Process Assets

DIAGNOSIS

Gap analysis, SWOT and future-state requirements

60 PROCESSES

Controlled final cross-functional baseline

RASCI

Matched responsibilities for every process

OPA BASELINE

Reusable company assets, not one-off project documents

3 METHODS

23 Email · 12 Jisr · 25 Odoo

EMAIL WORKBOOK

Operation and monitoring workbook for the 23 Email processes

SCOPE BOUNDARY

These outputs are a part of the company's Organizational Process Assets: reusable on every future project, department cycle and audit. Departmental SOPs, policies and detailed templates are developed, issued and maintained by the responsible department manager.

Each process is utilized through one of three application methods

EMAIL23	JISR12	ODOO25
PROCESS RECORDS • Shared activation email dated 10 May 2025 • Already published by mail • Process + RASCI	PROCESS RECORDS • Reflected and operated on the Jisr platform • Developed by the Saudi Elaf internal IT team, already published by mail • Process + RASCI	PROCESS RECORDS • Configured live implementation • Developed by Perfect Tech, already published by mail • Process + RASCI + application band

REQUIRED SEQUENCE AND EMAIL OPERATION

The report presents Email first, then Jisr, then Odoo. Within each method, processes are listed by owner department, and each process is assigned to exactly one method. The Email Application Operation and Monitoring Workbook is issued with the package to operate the Email group: a controlled transmission log per process code and a dashboard of issued, acknowledged and pending transmittals.

The complete approved process register

NO	CODE	APPROVED PROCESS	OWNER	METHOD	NO	CODE	APPROVED PROCESS	OWNER	METHOD
1	SE-QA-PRO-BSD-001	Tender Go / No Go	Business Develop...	ODOO	31	SE-QA-PRO-COM-001	Project Client Invoice	Commercial	ODOO
2	SE-QA-PRO-BSD-002	Company Prequalification Preparation fo...	Business Develop...	EMAIL	32	SE-QA-PRO-COM-002	Subcontractor Invoice	Commercial	ODOO
3	SE-QA-PRO-BSD-003	Events	Business Develop...	EMAIL	33	SE-QA-PRO-TEN-001	Project Cost Estimation (Job Costing)	Tendering	ODOO
4	SE-QA-PRO-BSD-004	Visitors' Hospitality	Business Develop...	JISR	34	SE-QA-PRO-TEN-002	Project Tender Preparation & Submission	Tendering	ODOO
5	SE-QA-PRO-BSD-005	Service Provider Request & Awarding (Su...	Business Develop...	ODOO	35	SE-QA-PRO-PRJ-001	Project Organization Chart	Projects	EMAIL
6	SE-QA-PRO-PCS-001	Project Awarding Announcement & Data Ha...	Project Controls	EMAIL	36	SE-QA-PRO-PRJ-002	Project Kickoff Internal Plan	Projects	EMAIL
7	SE-QA-PRO-PCS-002	Project (Construction) Baseline Schedule	Project Controls	EMAIL	37	SE-QA-PRO-PRJ-003	Daily Manpower	Projects	ODOO
8	SE-QA-PRO-PCS-003	Project (Construction) Cash Flow (Cash...	Project Controls	EMAIL	38	SE-QA-PRO-PRJ-004	Claims & Variation Orders	Projects	EMAIL
9	SE-QA-PRO-PCS-004	Projects (Construction) Daily Reports	Project Controls	EMAIL	39	SE-QA-PRO-PRJ-005	Procurement Plan (Schedule)	Projects	EMAIL
10	SE-QA-PRO-PCS-005	Projects (Construction) Periodical Repo...	Project Controls	ODOO	40	SE-QA-PRO-PRJ-006	Two-Month Look-Ahead (Construction Proj...	Projects	EMAIL
11	SE-QA-PRO-PCS-006	Project Resources Plan	Project Controls	EMAIL	41	SE-QA-PRO-FIN-001	Payment Request, Approval & Issuing	Finance	ODOO
12	SE-QA-PRO-PCS-007	Project Internal Cash Flow (Cash Out)	Project Controls	EMAIL	42	SE-QA-PRO-FIN-002	Petty Cash	Finance	ODOO
13	SE-QA-PRO-PCS-008	Project (Construction) Cost Control	Project Controls	ODOO	43	SE-QA-PRO-FIN-003	Projects Monthly Financial Report	Finance	ODOO
14	SE-QA-PRO-PCS-009	Project Closure Report	Project Controls	EMAIL	44	SE-QA-PRO-FIN-004	Projects Financial Planning	Finance	EMAIL
15	SE-QA-PRO-PCS-010	Company Master Projects Time Schedule	Project Controls	EMAIL	45	SE-QA-PRO-FIN-005	Department Budget Submission & Approval	Finance	ODOO
16	SE-QA-PRO-PCS-011	Company Master Projects Cash Flow (Cash...	Project Controls	EMAIL	46	SE-QA-PRO-ITS-001	Employee IT Custody Handover & Takeover	IT	JISR
17	SE-QA-PRO-CON-001	Subcontracting Contracts	Contracts	ODOO	47	SE-QA-PRO-ITS-002	Meetings (Inside HQ)	IT	JISR
18	SE-QA-PRO-CON-002	Projects Contracts Review	Contracts	EMAIL	48	SE-QA-PRO-ITS-003	IT Service or Repair	IT	JISR
19	SE-QA-PRO-PRC-001	Material Requisition	Procurement	ODOO	49	SE-QA-PRO-LOG-001	Car Requisition	Logistics	JISR
20	SE-QA-PRO-PRC-002	Subcontracting	Procurement	ODOO	50	SE-QA-PRO-LOG-002	Equipment Requisition	Logistics	ODOO
21	SE-QA-PRO-PRC-003	Supplier / Subcontractor Evaluation	Procurement	ODOO	51	SE-QA-PRO-LOG-003	Flight Requisition	Logistics	JISR
22	SE-QA-PRO-HUR-001	Employee Recruitment	Human Resources	EMAIL	52	SE-QA-PRO-LOG-004	Equipment Repair Requisition	Logistics	ODOO
23	SE-QA-PRO-HUR-002	Employee Replacement / Layoff / Interna...	Human Resources	JISR	53	SE-QA-PRO-WAH-001	Material Receiving, Addition, Storing...	Warehouse	ODOO
24	SE-QA-PRO-HUR-003	Employee Evaluation	Human Resources	JISR	54	SE-QA-PRO-WAH-002	Material Release from Store	Warehouse	ODOO
25	SE-QA-PRO-HUR-004	Employee Resignation	Human Resources	JISR	55	SE-QA-PRO-WAH-003	Subcontractor Material Record	Warehouse	ODOO
26	SE-QA-PRO-HUR-005	Employee Termination	Human Resources	EMAIL	56	SE-QA-PRO-WAH-004	Scrap Material Selling	Warehouse	ODOO
27	SE-QA-PRO-HUR-006	Payroll	Human Resources	JISR	57	SE-QA-PRO-WAH-005	Transfer Material Between Projects	Warehouse	ODOO
28	SE-QA-PRO-HUR-007	Annual Salaries Review / Increment	Human Resources	JISR	58	SE-QA-PRO-WAH-006	Store Emergency Opening	Warehouse	ODOO
29	SE-QA-PRO-HUR-008	Employee Development & Training	Human Resources	EMAIL	59	SE-QA-PRO-WAH-007	Warehouse & Project Material Monitoring	Warehouse	ODOO
30	SE-QA-PRO-HUR-009	Business Trip	Human Resources	JISR	60	SE-QA-PRO-QAS-001	Internal Auditing	Quality Assurance	EMAIL
EMAIL 23					JISR 12				
					ODOO 25				


APPROVED MAY 2025 · THE CODE PREFIX CARRIES THE OWNER DEPARTMENT · FULL DETAIL IN SECTION 6 OF THE CLOSURE REPORT

Every key person interviewed, and every session minuted

DATE	FUNCTION	KEY PERSON	SCOPE COVERED IN THE SESSION	MOM
26 May 2024	Tendering	Eng. Islam Adel	Department workflow, tender inputs, estimation, approvals and cross-functional dependencies	MOM
27 May 2024	Project Controls	Eng. Alaa Elaryan	Planning, cash-flow coordination, cost control, reporting and project interfaces	MOM
28 May 2024	Executive Management	Eng. Khaled Abdallah, Deput...	Strategy, governance, delegation, operating model and company-wide gaps	MOM
30 May 2024	Business Development	Eng. Abdelrahman Gamal	Opportunity sourcing, tender handover, events, hospitality and governance gaps	MOM
30 May 2024	Facility Management	Eng. Ahmed Magdy	FM workflows, maintenance needs, mobilization, staffing and interdepartmental interfaces	MOM
1 Jun 2024	Procurement	Eng. Mohamed Abdelrahman	Material and subcontract cycles, records, approvals, delivery controls and supplier management	MOM
1 Jun 2024	Projects - Riyadh	Eng. Ibrahim Elzomor	Site delivery, resources, stores, reporting, controls, closeout and support functions	MOM
2 Jun 2024	IT	Eng. Mohamed Abdelhamid	IT custody, service and repair, systems, records, access and support processes	MOM
3 Jun 2024	Accounting	Mr. Mohamed Omar	Accounting structure, project accounting, petty cash, records and coordination controls	MOM
3 Jun 2024	Human Resources	Mr. Yaser Abed	Recruitment, onboarding, evaluation, payroll, training and Jisr-supported services	MOM
4 Jun 2024	Catering	Eng. Mubashir Abbas	Business development, tendering, operations, procurement, logistics and HR interfaces	MOM
4 Jun 2024	Logistics	Mr. Fahd	Requests, approvals, travel, communications, services and cost allocation interfaces	MOM
5 Jun 2024	Finance / Executive Support	Mr. Mohamed Shaker	Banking interfaces, collections, planning, records and organizational roles	MOM
5 Jun 2024	Projects - NEOM / Oxagon / Si...	Eng. Mohamed Awad	Project delivery, QA/QC, HSE, manpower, stores, variations and controls	MOM
5 Jun 2024	QA/QC	Eng. Ahmed Hassan	Quality planning, project controls, material inspection, process governance and auditing gaps	MOM
6 Jun 2024	Projects - NEOM / Vertical Fa...	Eng. Mohamed Afifi	Resources, site systems, logistics, stores, technical support and contract interfaces	MOM
3 Jul 2024	Technical Office	Eng. Mohamed Elsayy	Design and tender support, outsourcing, schedules, technical records and closeout support	MOM

17 KEY-PERSON SESSIONS · 17 CONTROLLED MOM RECORDS · 26 MAY TO 3 JULY 2024 · REGISTERED IN APPENDIX A AND REPRODUCED IN APPENDIX F

Every handover bundle links the approved process to responsibility and application

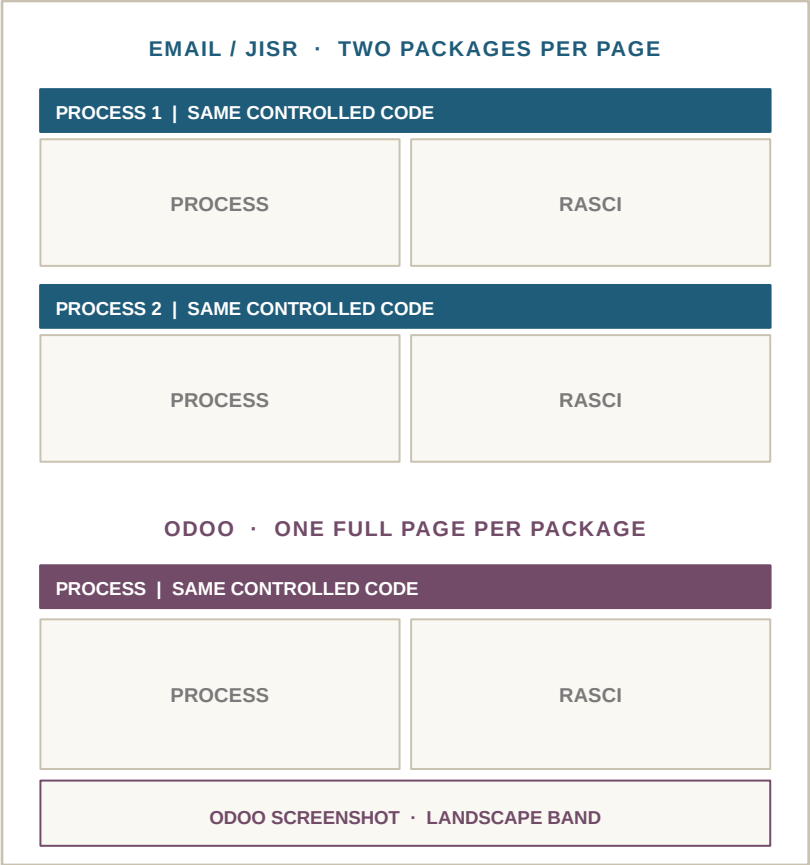

EMAIL AND JISR PACKAGES

Two packages per A4 page. Each shows two visuals, left to right: the approved process flowchart, then the matching approved RASCI matrix.

ODOO PACKAGES

One full A4 page each. Process and RASCI side by side at the top, then a full-width landscape band carrying the live Odoo screenshot or screenshots.

CODE INTEGRITY

Codes run sequentially within each owner department with no gaps, and match across the workflow, the RASCI matrix and every cross-reference.

DEPARTMENTAL DOCUMENTS

Any required SOP, policy or detailed template is developed, issued and maintained by the responsible department manager, and is cross-referenced only.

What the scope was, and what was added on top of it

THE APPROVED SCOPE

Develop and submit the processes	Diagnosis, gap analysis and stakeholder interviews, then the 60 cross-functional processes with their approved workflows and RASCI role interfaces, submitted for approval.
Support the implementation	Implementation through Email, Jisr and Odoo: the Email application with its Operation and Monitoring Workbook, the Jisr reflection with the internal IT team, and the Odoo configuration alignment, verified after joining Saudi Elaf and leading the ERP transformation.

DELIVERED BEYOND THE APPROVED SCOPE

Company organization chart	Developed from the gap analysis in three phases, from department managers up to C-suite level, so the structure carries the new cross-functional roles.
Controlled process repository	A company asset document of 139 pages: all 60 workflows and RASCI matrices filed by owner department, with a clickable contents and a register per department.
Departmental participation matrix	One grid showing, for every process, the owner department and every unit that takes part through it, plus a page per unit.

SUBMITTING THE PROCESSES AND SUPPORTING THEIR IMPLEMENTATION IS THE SCOPE · THE THREE ITEMS ABOVE WERE ADDED AT NO CHANGE TO IT

What is handed over, and where the controlled master lives

Executive Closure Presentation

PowerPoint and PDF · 13 slides

Closure & Handover Report

PDF and Word · 158 pages

Process Repository by Owner Department

PDF · 139 pages, by the 13 owner departments

Departmental Participation Matrix

PDF and Excel · 18 pages

Approved Process Packages

PDF · 60 files, 120 controlled pages

Email Application Operation and Monitoring Workbook

Excel · register, transmission log and dashboard

Odoo Screenshot Naming List

Excel · controlled naming of the application records

Process Repository, A3 Binder Edition


PDF · 139 print-ready sheets, issued as a soft copy

CONTROLLED REPOSITORY

Every deliverable above is held in the controlled repository:

<https://amr7adary.github.io/Saudi-Elaf-Processes-Repository/>

Closure transfers Saudi Elaf's approved internal-use process baseline

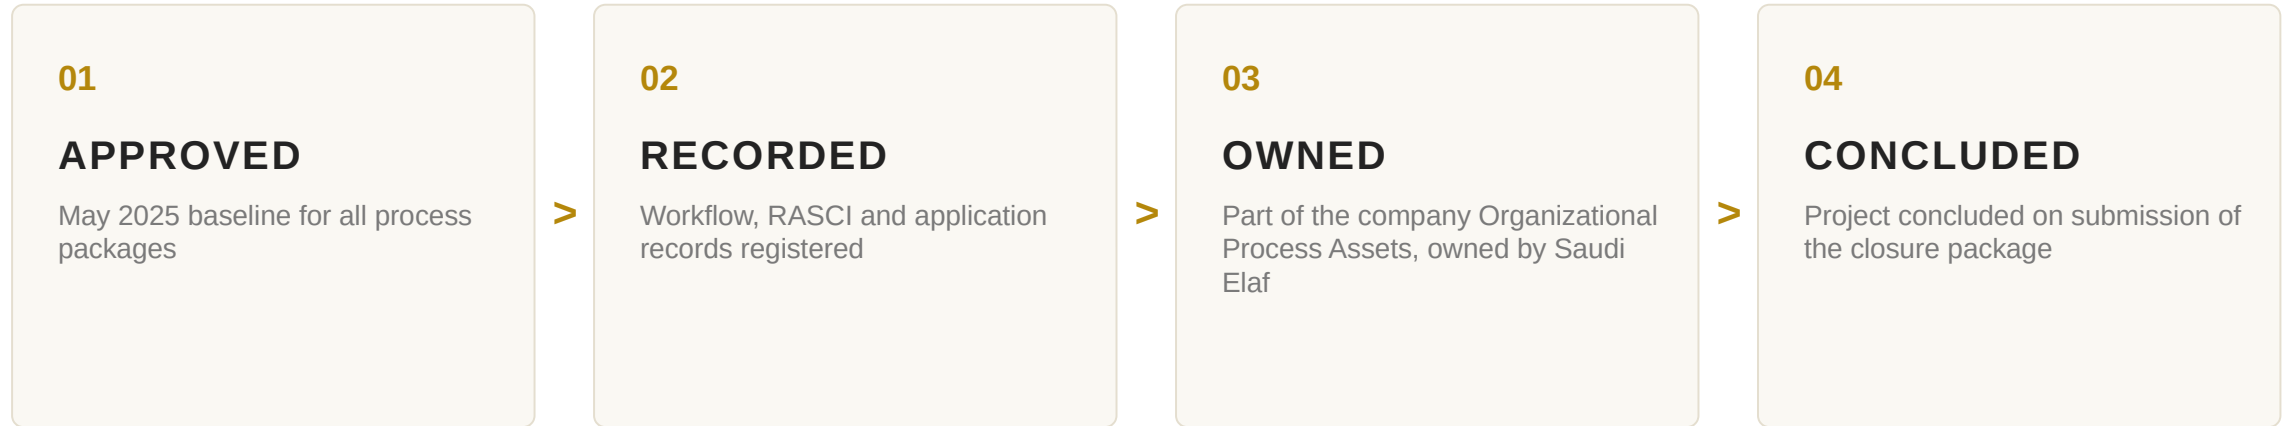

FINAL CLOSURE STATEMENT

The outsourced technical scope is complete. The 60-process baseline, the approved process and RASCI packages, the shared Email activation reference, the Jisr-platform reflection, the Odoo screenshots and the monitoring tools are handed over to Saudi Elaf Company as a part of its Organizational Process Assets, for reuse and continued governance. It was agreed on the October 2024 job offer of Operations Area Manager that the remaining project work and the implementation would be carried out after joining. Eng. Amr Elhadary joined Saudi Elaf in November 2024 and led the ERP transformation project, supporting and verifying that Odoo reflects the approved cross-functional processes, which has been completed.

CONTROLLED REPOSITORY · [HTTPS://AMR7ADARY.GITHUB.IO/SAUDI-ELAF-PROCESSES-REPOSITORY/](https://amr7adary.github.io/saudi-elaf-processes-repository/)
